BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

**Date :** 25.04.2022

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| | | | | | | | Bill Status : 1st And Final Bill | |
| 1 | Earthwork in surface excavation in ordinary soil for levelling and lowering the ground manually (other than foundation of buildings, culverts, road drains and trenches of pipe lines and cables) and removing the excavated stuff to a distance not exceeding 50 m and lift upto 1.5m, excavated surface levelled and neatly dressed, disposed earth to be levelled after breaking of clods and nealty dressed as per specifications Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **For Toilet** | Cum | | | | | | |
| | **Levelling** | | 1 | 11.00 | 5.35 | 0.15 | **8.83** | |
| | | | | | | | **8.83** | |
| | | | | | | **Qty Payable In This Bill** | **8.83** | |
| 2 | Earthwork excavation for foundation of buildings, culverts, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 1.5m in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50m. after breaking of clods complete as per specifications.Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **For Toilet** | Cum | | | | | | |
| | **For Footing** | | 8 | 1.50 | 1.50 | 2.00 | **36.00** | |
| | **For Foundation** | | 2 | 10.65 | 0.90 | 0.90 | **17.25** | |
| | | | 2 | 5.35 | 0.90 | 0.90 | **8.67** | |
| | | | 6 | 1.45 | 0.60 | 0.60 | **3.13** | |
| | **Pipeline** | | | | | | | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 30.00 | 0.60 | 0.60 | **10.80** | |
| | | | 1 | 18.00 | 0.60 | 0.60 | **6.48** | |
| | **Over Burden Earth** | | 1 | 32.00 | 10.00 | 1.40 | **448.00** | |
| | **Toilet Front** | | 1 | 10.65 | 2.00 | 0.30 | **6.39** | |
| | | | | | | **Total Work Done** | **644.72** | |
| | | | | | | **Qty Payable Upto 125 %** | **299.50** | |
| | | | | | | **Qty Payable Above 125 %** | **345.22** | |

Assistant Engineer
Ward No 17

Pangkamma
Contractor Representive

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara Palike

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 02.05.2022

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 3 | KSRB 4-1.3 : Providing and laying in position plain cement concrete of mix M7.5 with OPC cement @ 180 kgs, with 40mm and down size graded granite metal coarse aggregates @ 0.85 cum and fine aggregates @ 5.75 cum machine mixed, concrete laid in layers not exceeding 15 cms, thick, well compacted, in foundation and plinth, including cost of all materials, labour, HOM of machinery, curing complete as per specification. | | | | | | | |
| | **For Toilet** | Cum | | | | | | |
| | **For Footing** | | | | | | | |
| | **For Foundation** | | 8 | 1.50 | 1.50 | 0.15 | **2.70** | |
| | | | 2 | 10.65 | 0.90 | 0.15 | **2.88** | |
| | | | 2 | 5.35 | 0.90 | 0.15 | **1.44** | |
| | **Pipeline** | | 6 | 1.45 | 0.60 | 0.15 | **0.78** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | | | 1 | 30.00 | 0.60 | 0.15 | **2.70** | |
| | **Toilet Front** | | 1 | 18.00 | 0.60 | 0.15 | **1.62** | |
| | | | 1 | 10.65 | 2.00 | 0.15 | **3.20** | |
| | | | | | | **Total Work Done** | **42.32** | |
| | | | | | | **Qty Payable Upto 125 %** | **34.50** | |
| | | | | | | **Qty Payable Above 125 %** | **7.82** | |
| 4 | Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @320kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878cum and fine aggregates @ 0.459cum, with superplastisiser @ 3lts confirming to IS9103-1999 Reaffirmed-2008, machine mixed, concrete laid in layers not exceeding 15cms thick, vibrated for all works in foundation plinth and ground floor level for roof slabs, staircase, lintles, retaining walls, return walls, walla (any thickness) including attached plasters, columns, piers, abutments, pillars, posts, structs, buttresses, string or lacing courses, parpets, coping, bed blocks, anchor, plain window cills, fillets etc., including cost of all materials, labour, HOM of machinery, curing complete as per specification. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **For Toilet** | Cum | | | | | | |
| | **For Footing** | | 8 | 1.20 | 1.20 | 0.45 | **5.18** | |
| | Pedestal | | 8 | 0.60 | 0.60 | 0.75 | **2.16** | |
| | Column Upto Plinth | | 8 | 0.23 | 0.23 | 0.65 | **0.28** | |
| | | | | | | **Total Work Done** | **7.62** | |
| | | | | | | **Qty Payable In This Bill** | **7.62** | |

Junior Engineer
Ward No 17

Contractor Representive

Asst. Executive Engineer
Yeshwanthpur Sub Division
Bruhat Bangalore Mahanagara Palike

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 30.05.2022

Bill Status : 1st And Final Bill

| Item No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 5 | Providing and removing centering, shuttering, strutting, propping etc., an removal of form work for sides & soffits of beams, beam hauncing cantilever girders, bressumers & lintels & not exceeding 1.0 in depth including cost of all materials, labour complete as per specifications. | | | | | | | |
| | **For Toilet** | Sqm | | | | | | |
| | **For Footing** | | | | | | | |
| | **Pedestal** | | 8 | 4.80 | | 0.45 | 17.28 | |
| | **Column Upto Plinth** | | 8 | 2.40 | | 0.75 | 14.40 | |
| | Plinth Beam | | 8 | 0.92 | | 0.65 | 4.78 | |
| | | | 6 | 10.65 | | 0.45 | 28.76 | |
| | | | 6 | 5.35 | | 0.45 | 14.45 | |
| | Wall Beams | | 12 | 1.45 | | 0.30 | 5.22 | |
| | | | 6 | 10.65 | | 0.45 | 28.76 | |
| | | | 6 | 5.35 | | 0.45 | 14.45 | |
| | | | 12 | 1.45 | | 0.45 | 7.83 | |
| | | | | | | **Total Work Done** | 135.91 | |
| | | | | | | **Qty Payable In This Bill** | 135.91 | |
| 6 | Providing and laying in position reinforced cement cocnrete of design mix M20 with OPC cement @ 27.20 Kgs with 12mm & down sizes graded grantie metal coarse aggregated @ 0.5865 cum & fine aggregates, @ 0.391 Cum with super super plastisiser @ 0.225 Ltrs maichine mixed well compacted plain chajja 8.50 Cms avg thickness, up to ground floor level including removing centering, shuttering, strutting, propping etc., and removal of form work for cost of all materials, laobur HOM of machinary, curing complete as per specification.Ground floor | | | | | | | |
| | Plinth Beam | | | | | | | |
| | | | 3 | 10.65 | 0.23 | 0.45 | 3.31 | |
| | | | 3 | 5.35 | 0.23 | 0.45 | 1.66 | |
| | | | 6 | 1.45 | 0.23 | 0.30 | 0.60 | |
| | Wall Beams | | | | | | | |
| | | | 3 | 10.65 | 0.23 | 0.60 | 4.41 | |
| | | | 3 | 5.35 | 0.23 | 0.60 | 2.21 | |
| | | | 6 | 1.45 | 0.23 | 0.60 | 1.20 | |
| | | | | | | **Total Work Done** | 13.39 | |
| | | | | | | **Qty Payable Upto 125 %** | 8.13 | |
| | | | | | | **Qty Payable Above 125 %** | 5.27 | |
| 7 | Providing TMT Steel reinforcement for RCC works including straightening, cutting, bending, hooking, placing in position lapping and / or welding wherever required, tieng with binding wire and anchoring to the adjoining members wherever necessary, complete as per design (laps, hooks and wastage shall not be measured and paid) cost of all materials, labour, HOM of machineries etc., complete as per specifications. Specification No.KBS 4.6.3. FOR TMT Bars Fe- 500 Ground Floor Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | | Tonne | | | | | | |
| | **Qty Vide From Calculation Sheet** | | | | | | | |
| | | | | | | | 2.84 | |
| | | | | | | **Total Work Done** | 2.84 | |
| | | | | | | **Qty Payable In This Bill** | 2.84 | |

Asst. Engineer
Ward No 17

Contractor Representive

Executive Engineer
Yeshwanthpur Sub Division
Bruhat Bangalore Mahanagara P

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 14.05.2021

Bill Status : 1st And Final Bill

| No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 8 | Providing & Constructing Granite/ trap/basalt size stone Masonary in basement with Cement morter 1:8 edges of stone chistle dressed in courses not less than 15 cms high, bond stones at two mtr apart in each course including cost of all materials, labour, curing complete as per specifications Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | For Foundation | Sqm | | | | | | |
| | **1st Steps** | | 2 | 10.65 | 0.75 | 0.60 | **9.59** | |
| | | | 2 | 5.35 | 0.75 | 0.60 | **4.82** | |
| | | | 6 | 1.45 | 0.75 | 0.60 | **3.92** | |
| | 2nd Steps | | | | | | | |
| | | | 2 | 10.65 | 0.60 | 0.60 | **7.67** | |
| | | | 2 | 5.35 | 0.60 | 0.60 | **3.85** | |
| | | | 6 | 1.45 | 0.60 | 0.60 | **3.13** | |
| | | | 2 | 10.65 | 0.45 | 0.40 | **3.83** | |
| | | | 2 | 5.35 | 0.45 | 0.40 | **1.93** | |
| | | | 6 | 1.45 | 0.45 | 0.40 | **1.57** | |
| | | | | | | **Total Work Done** | **40.29** | |
| | | | | | | **Qty Payable In This Bill** | **40.29** | |
| 9 | Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20 cms. In depth, compacting each deposited layer by ramming after watering with lead upto 50 m. and lift upto 1.5m. Inluding cost of all labour complete as per speicifications.Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | | Cum | | | | | | |
| | **Ew Qty** | | | | | | **644.72** | |
| | **Deduct Bed concrete** | | | | | | **-42.32** | |
| | **Deduct Column Qty** | | | | | | **-7.62** | |
| | **Deduct SSM Qty** | | | | | | **-32.97** | |
| | **For Flooring** | | 1 | 10.65 | 5.35 | 0.60 | **34.19** | |
| | | | | | | **Total Work Done** | **596.00** | |
| | | | | | | **Qty Payable Upto 125 %** | **119.88** | |
| | | | | | | **Qty Payable Above 125 %** | **476.13** | |

Asst. Executive Engineer
Ward No 17

Contractor Representive

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara Palike

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 19.05.2021

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 10 | Providing and constructing Pre cast solid blocks with Compressive strength not less than 35 kg/ sqm with cement morter 1:4 masonary ( quion, Jamb, closer block) with solid concrete blockx of size 40 x 15 x 20 cms confirming to IS 2185/1965 in super structures including cost of materials, labour charges, scaffolding, curing complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift. | | | | | | | |
| | For Toilet | | | | | | | |
| | **For Wall** | Cum | | | | | | |
| | | | 2 | 10.65 | | 3.10 | 66.03 | |
| | **Dedct** | | 3 | 5.35 | | 3.10 | 49.76 | |
| | **RS** | | | | | | | |
| | V | | -1 | 3.30 | | 2.10 | -6.93 | |
| | | | -6 | 0.60 | | 0.60 | -2.16 | |
| | | | | | | **Total Work Done** | 106.70 | |
| | | | | | | **Qty Payable In This Bill** | 106.70 | |
| 11 | Providing & constructing non load bearing walls cemect concrete solid blocks with compressive strength not less than 35 kg/sqm with cement morter 1:4 ( jamb, closer blocks ) with blocks of size 40X10X20. (LXBXH) confirming to I.S. : 2185/1965 in super structure including cost of materials, labour charges, scaffolding, curing complete as per specification.Complete as per the direction of Engineer in Charge with all lead and Lift. | | | | | | | |
| | **For Toilet** | Sqm | | | | | | |
| | **Partion Wall** | | | | | | | |
| | | | 6 | 1.45 | | 3.10 | 26.97 | |
| | | | 2 | 10.65 | | 3.10 | 66.03 | |
| | Dedct | | | | | | | |
| | **D** | | -5 | 0.75 | | 2.10 | -7.88 | |
| | | | -2 | 1.20 | | 2.10 | -5.04 | |
| | | | | | | **Total Work Done** | 80.09 | |
| | | | | | | **Qty Payable Upto 125 %** | 37.88 | |
| | | | | | | **Qty Payable Above 125 %** | 42.21 | |

Contractor Represented

Asst. Executive Engineer
Yeshwanthpur Sub Division
Bruhat Bangalore Mahanagara Palike

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 23.05.2022

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 12 | Providing 18mm thick cement plaster in single coat with cement mortor 1:3 to Brick masonary including rounding off corners wherver required smooth rendering,: Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **Outer Wall Plastering** | m | | | | | | |
| | | | 2 | 10.65 | | 3.10 | 66.03 | |
| | | | 2 | 5.35 | | 3.10 | 33.17 | |
| | | | -1 | 3.30 | | 2.10 | -6.93 | |
| | | | -7 | 0.60 | | 0.60 | -2.52 | |
| | Toilet Block 2 | | | | | | | |
| | | | 1 | 5.70 | | 3.00 | 17.10 | |
| | | | 1 | 12.20 | | 3.00 | 36.60 | |
| | | | -1 | 0.90 | | 3.10 | -2.79 | |
| | | | -3 | 0.60 | | 0.60 | -1.08 | |
| | Toilet Block 3 | | | | | | | |
| | | | 1 | 5.70 | | 3.00 | 17.10 | |
| | | | 1 | 12.20 | | 3.00 | 36.60 | |
| | | | -1 | 0.90 | | 3.10 | -2.79 | |
| | | | -3 | 0.60 | | 0.60 | -1.08 | |
| | Toilet Block 4 | | | | | | | |
| | | | 1 | 3.00 | | 3.00 | 9.00 | |
| | | | 1 | 3.20 | | 3.00 | 9.60 | |
| | | | -1 | 0.90 | | 3.10 | -2.79 | |
| | | | -1 | 0.60 | | 0.60 | -0.36 | |
| | | | | | **Total Work Done** | | 204.86 | |
| | | | | | **Qty Payable In This Bill** | | 204.86 | |
| 13 | Providing 18mm thick cement plaster in single coat with cement mortor 1:4, to brick masonry including rounding off corners wherver required smooth rendering,: Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.( internal). Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **Inner Wall Plastering** | Sqm | | | | | | |
| | | | 6 | 10.65 | | 3.10 | 198.09 | |
| | | | 4 | 5.35 | | 3.10 | 66.34 | |
| | | | 12 | 1.45 | | 3.10 | 53.94 | |
| | Dedct | | | | | | | |
| | D | | -2 | 1.20 | | 2.10 | -5.04 | |
| | D2 | | -7 | 0.75 | | 2.10 | -11.03 | |
| | V | | -7 | 0.60 | | 0.60 | -2.52 | |
| | | | | | | | | |
| | Toilet Block 2 | | 1 | 5.60 | | 3.00 | 16.80 | |
| | | | 1 | 12.20 | | 3.00 | 36.60 | |

Contractor Representive

Asst. Executive Engineer
Yeshwanthpura Sub Div.
Bruhat Bangalore Mahanagara Palike

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 23.05.2022

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| | | | -1 | 0.90 | | | | |
| | | | -3 | 0.60 | | | | |
| | Toilet Block 3 | | | | | 3.10 | -2.79 | |
| | | | | | | 0.60 | -1.08 | |
| | | | 1 | 5.60 | | | | |
| | | | 1 | 1.20 | | | | |
| | | | | | | 3.00 | 16.80 | |
| | | | | | | 3.00 | 3.60 | |
| | | | -1 | 0.90 | | | | |
| | | | -3 | 0.60 | | | | |
| | Toilet Block 4 | | | | | 3.10 | -2.79 | |
| | | | | | | 0.60 | -1.08 | |
| | | | 2 | 3.00 | | | | |
| | | | 2 | 3.20 | | | | |
| | | | | | | 3.00 | 18.00 | |
| | | | | | | 3.00 | 19.20 | |
| | | | -1 | 0.90 | | | | |
| | | | -1 | 0.60 | | | | |
| | | | | | | 3.10 | -2.79 | |
| | | | | | | 0.60 | -0.36 | |
| | | | | | Total Work Done | | 399.90 | |
| | | | | | Qty Payable In This Bill | | 399.90 | |
| 14 | Providing 12mm thick cement plaster in single coat with cement mortor 1:3, to ceiling including rounding off corners wherver required smooth rendering,: Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. GG. Complete as per the direction of Engineer in Charge with all lead and Lift. Complete as per the direction of Engineer in Charge with all lead and Lift | Sqm | | | | | | |
| | Toilet Block 2 | | | | | | | |
| | | | 1 | 12.20 | 2.35 | | 28.67 | |
| | | | 2 | 5.70 | 3.30 | | 37.62 | |
| | Toilet Block 3 | | | | | | | |
| | | | 1 | 12.20 | 2.35 | | 28.67 | |
| | | | 2 | 5.70 | 3.30 | | 37.62 | |
| | Toilet Block 4 | | | | | | | |
| | | | 2 | 4.85 | | 2.70 | 26.19 | |
| | | | 2 | 5.80 | | 2.70 | 31.32 | |
| | | | -4 | 0.75 | | 3.10 | -9.30 | |
| | | | -2 | 0.60 | | 0.60 | -0.72 | |
| | | | | | Total Work Done | | 180.07 | |
| | | | | | Qty Payable In This Bill | | 180.07 | |

Assistant Engineer
Ward No 17

Contractor Represented

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 30.06.2022

Bill Status : Ist And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 15 | Providing INTEGRAL CRYSTALINE Waterproofing treatment to the sunken portion of toilets. Using Crystalline Slurry of approved make @ 1.40 kg per SQM in two coats (0.7 Kg per coat) confirming to ASTM S 1202 & DINV 18998 standards. Complete as per the direction of Engineer in Charge with all lead and Lift. | | | | | | | |
| | Toilet Block 2 | Sqm | | | | | | |
| | | | 1 | 12.20 | 2.35 | | 28.67 | |
| | | | 2 | 5.70 | 3.30 | | 37.62 | |
| | Toilet Block 3 | | | | | | | |
| | | | 1 | 12.20 | 2.35 | | 28.67 | |
| | | | 2 | 5.70 | 3.30 | | 37.62 | |
| | Toilet Block 4 | | | | | | | |
| | | | 2 | 4.85 | 5.80 | | 56.26 | |
| | | | | | | Total Work Done | 188.84 | |
| | | | | | | Qty Payable In This Bill | 188.84 | |
| 16 | Providing and fixing of factorymade 30 mm P.V.C door frame of size 50x47 mm with a wall thickness of 5 mm made out of extrued 5 mm rigid PVC foamsheet metered cut at cornwers & jointed 2 nos 150 mm long brackets of 15 x 15 mm MS Square tube, the entire door frame to be reinforced with 19 x 19 m square tube of 19 gauge. the door frame to be fixed to the wall using MS screws of 65 /80 mm size complete as per manufacturers specification& directions of Engineer in charge. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | Toilet | Cum | | | | | | |
| | | | 9 | 5.70 | | | 51.30 | |
| | | | | | | Total Work Done | 51.30 | |
| | | | | | | Qty Payable In This Bill | 51.30 | |
| 17 | Providing & fixing 30mm thick factory made rigid foam Panelled Door Shutters made from M.S. tube of 19 gauge thickness, size 19 x 19mm for styles and 15 x 15mm for top and bottom rails, covered with heat moulded PVC channel of 5mm thick sheet & 30 x 50mm wide to form styles & 5mm thick & 75mm wide PVC Sheets for top rail, lock rail & bottom rail on either side & 5mm thick 20mm wide PVC sheet as gap insert for top rail & bottom rail, Panelling of 5mm thick PVC sheet fitted in the M.S. Frame, Sealed to the styles & rails with 5 x 30mm PVC sheet beading on either side & joined together with solvent cement adhesive etc., Complete as per manufacturers specification & direction of Engineer-in-charge fixed to | | | | | | | |
| | Toilet | Cum | | | | | | |
| | | | 9 | 0.75 | | 2.10 | 14.18 | |
| | | | | | | Total Work Done | 14.18 | |
| | | | | | | Qty Payable In This Bill | 14.18 | |

Engineer
No 17

Contractor Represenative

Asst. Executive Engin
Yeshwanthpura Sub Div
Bruhat Bangalore Mahanaga

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 30.06.2022

Bill Status : 1st And Final Bill

| S No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 18 | Providing ceramic tiles of approved make, shade and size for flooring, treads of steps and landings laid on a bed of 12mm thick cement mortor 1:3 mix, flush pointing with white cement using colour pigment, including cost of materials, labour, curing, complete as per specifications. size 30x30cms. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | For Toilet | Cum | | | | | | |
| | | | 1 | 10.65 | 1.15 | | 12.25 | |
| | | | 1 | 10.65 | 0.95 | | 10.12 | |
| | Skirting | | 7 | 1.45 | 1.10 | | 11.17 | |
| | Toilet Block 2 | | 1 | 40.60 | | 0.15 | 6.09 | |
| | | | 1 | 12.20 | 2.35 | | 28.67 | |
| | | | 2 | 5.70 | 3.30 | | 37.62 | |
| | Toilet Block 3 | | | | | | | |
| | | | 1 | 12.20 | 2.35 | | 28.67 | |
| | | | 2 | 5.70 | 3.30 | | 37.62 | |
| | Toilet Block 4 | | | | | | | |
| | | | 1 | 3.10 | 8.80 | | 27.28 | |
| | | | 1 | 1.75 | 5.80 | | 10.15 | |
| | | | | | | Total Work Done | 209.63 | |
| | | | | | | Qty Payable In This Bill | 209.63 | |
| 19 | Providing skirting, dado, rises of steps with colour glazed tiles on 10mm thick cement plaster 1:3 and jointed with white cement slurry over rough plaster surface (excluding cost of rough plastered surface which should be measured and paid separately) using glazed tiles of approved make and size including cost of materials, labour, complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | Wall Tiles | Sqm | | | | | | |
| | WC | | 7 | 5.10 | | 1.50 | 53.55 | |
| | Dect | | -7 | 0.75 | | 2.10 | -11.03 | |
| | ALRROUND Wall | | 1 | 32.00 | | 2.70 | 86.40 | |
| | Toilet Block 2 | | 2 | 9.70 | | 1.50 | 29.10 | |
| | | | 2 | 16.30 | | 1.50 | 48.90 | |
| | | | 4 | 5.40 | | 1.50 | 32.40 | |
| | Deduction | | | | | | | |
| | D | | -2 | 1.20 | | 1.50 | -3.60 | |
| | D1 | | -4 | 0.90 | | 1.50 | -5.40 | |
| | Open | | -2 | 1.20 | | 1.50 | -3.60 | |

Contractor Representive

Asst. Executive Engr
Yeshwanthpura Sub-Div
Bruhat Bangalore Mahanaga

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 30.06.2022

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| | R S | | -2 | 3.30 | | 1.50 | -9.90 | |
| | Toilet Block 3 | | 2 | 9.70 | | | | |
| | | | 2 | 16.30 | | 1.50 | 29.10 | |
| | Deduction | | 4 | 5.40 | | 1.50 | 48.90 | |
| | D | | | | | 1.50 | 32.40 | |
| | D1 | | -2 | 1.20 | | | | |
| | Open | | -4 | 0.90 | | 1.50 | -3.60 | |
| | R S | | -2 | 1.20 | | 1.50 | -5.40 | |
| | | | -1 | 3.30 | | 1.50 | -3.60 | |
| | Toilet Block 4 | | | | | 1.50 | -4.95 | |
| | | | 4 | 5.40 | | | | |
| | | | 1 | 8.00 | | 1.50 | 32.40 | |
| | Deduction | | 4 | 1.75 | | 1.50 | 12.00 | |
| | D | | | | | 1.50 | 10.50 | |
| | D1 | | -2 | 1.20 | | | | |
| | | | -4 | 0.75 | | 1.50 | -3.60 | |
| | | | | | | 1.50 | -4.50 | |
| | | | | | Total Work Done | | 356.48 | |
| | | | | | Qty Payable Upto 125 % | | 100.63 | |
| | | | | | Qty Payable Above 125 % | | 255.85 | |

20 Providing and applying two coats with oil bound washable distemper of approved brand and shade on wall surface including priming coat with distemper primer after throughly brooming the surface free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour, complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift.

| | | | | | | | | |
|---|---|---|---|---|---|---|---|---|
| | For Inside | Cum | | | | | | |
| | Item Wide From | 13 | | | | | | |
| | | | | | | | 399.90 | |
| | | | | | Total Work Done | | 399.90 | |
| | | | | | Qty Payable In This Bill | | 399.90 | |

21 Water proof cement paint KSRB 15-16.1 : Providing and finishing external walls in two coats with waterproof cement paint with primer of approved brand and shade to give an even shade after throughly brooming the surface to remove all dirt and loose powdered material, free from mortar drops and other foreign matter cost of materials, labour, complete as per specifications. (P.No.124/15.53.2) '--do with Primer-- GG. Complete as per the direction of Engineer in Charge with all lead and Lift

| | | | | | | | | |
|---|---|---|---|---|---|---|---|---|
| | For Outer Wall | Cum | | | | | | |
| | Item Wide From | | | | | | 204.86 | |
| | | | | | Total Work Done | | 204.86 | |
| | | | | | Qty Payable In This Bill | | 204.86 | |

Contractor Representive

Asst. Executive Engineer
Yeshwanthpur Sub Division
Bruhat Bangalore Mahanagara P

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 30.06.2022

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 23 | Providing and fixing white vitreous china clay, water closet Indian type (Squatting pan) of size 580mm with footrests, 100mm S or P trap, (approved make) cutting and making good the wall and floor wherever required, including cost of materials, labour complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **Closet** | No's | | | | | | |
| | | | 14 | | | | | |
| | | | | | | | 14.00 | |
| | | | | | | **Total Work Done** | 14.00 | |
| | | | | | | **Qty Payable In This Bill** | 14.00 | |
| 23 | Providing and fixing white vitreous china clay, flat back, lipped front urinal basin of 430x260x350mm with 5 litres PVC automatic flushing cistern, C.I / M.S brackets, standard flush pipe and C.P. brass spreaders with brass unions and G.I. clamps complete painting of fittings and brackets, cutting and making good the wall and floor wherever required, including cost of materials, labour complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **Urinal** | Each | | | | | | |
| | | | 14 | | | | | |
| | | | | | | | 14.00 | |
| | | | | | | **Total Work Done** | 14.00 | |
| | | | | | | **Qty Payable In This Bill** | 14.00 | |
| 24 | Providing & fixing CI Nahani trap of approved make confirming to ISI specification and construction of cistren in M 15 as per directions. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **Urinal** | Each | | | | | | |
| | | | 10 | | | | | |
| | | | | | | | 10.00 | |
| | | | | | | **Total Work Done** | 10.00 | |
| | | | | | | **Qty Payable In This Bill** | 10.00 | |
| 25 | Providing and fixing in position CP bib cock of approved quality 20 mm nominal bore including cost of all materials, labour and HOM of equipments with alll leads complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **Urinal** | Each | | | | | | |
| | | | 10 | | | | | |
| | | | | | | | 10.00 | |
| | | | | | | **Total Work Done** | 10.00 | |
| | | | | | | **Qty Payable In This Bill** | 10.00 | |

Contractor Represente

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara Pal

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 30.06.2021

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 26 | Providing and fixing to wall, ceiling and floor , Medium density polyethylene pipes 6.00 kgf /sqcm working pressure | | | | | | | |
| | **Urinal** | Mtr | | | | | | |
| | | | 1 | 65.00 | | | | |
| | | | | | | | 65.00 | |
| | | | | | | **Total Work Done** | 65.00 | |
| | | | | | | **Qty Payable Upto 125 %** | 20.00 | |
| | | | | | | **Qty Payable Above 125 %** | 45.00 | |
| 27 | Providing and fixing to wall, ceiling and floor , Medium density polyethylene pipes 6.00 kgf /sqcm working pressure | | | | | | | |
| | **Urinal** | Mtr | | | | | | |
| | | | 1 | 62.00 | | | | |
| | | | | | | | 62.00 | |
| | | | | | | **Total Work Done** | 62.00 | |
| | | | | | | **Qty Payable Upto 125 %** | 35.00 | |
| | | | | | | **Qty Payable Above 125 %** | 27.00 | |
| 28 | Providing and fixing to wall, ceiling and floor , Medium density polyethylene pipes 6.00 kgf /sqcm working pressure | | | | | | | |
| | **Urinal** | Mtr | | | | | | |
| | | | 1 | 72.00 | | | | |
| | | | | | | | 72.00 | |
| | | | | | | **Total Work Done** | 72.00 | |
| | | | | | | **Qty Payable Upto 125 %** | 25.00 | |
| | | | | | | **Qty Payable Above 125 %** | 47.00 | |
| 29 | Providing and fixing to wall, ceiling and floor chlorinated poly vinyl chloride ( CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all cpvc plain and brasss threaded fittings including fixing thepipes with the clamp at 1.00mtr spacing . This includes joining of pipes fittings with one set of cpvc solvent cement and testing of joints complete ( Internal works ) ( Concealed work including cutting chases and good the walls etc.)A)15mm dia pipe nominal OD pipes Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **For Toilet** | Mtr | | | | | | |
| | | | 1 | 90.00 | | | | |
| | | | | | | | 90.00 | |
| | | | | | | **Total Work Done** | 90.00 | |
| | | | | | | **Qty Payable Upto 125 %** | 15.00 | |
| | | | | | | **Qty Payable Above 125 %** | 75.00 | |

Contractor Represented

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 30.06.2022

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 30 | Providing and fixing to wall, ceiling and floor chlorinated poly vinyl chloride ( CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all cpvc plain and brasss threaded fittings including fixing thepipes with the clamp at 1.00mtr spacing . This includes joining of pipes fittings with one set of cpvc solvent cement and testing of joints complete ( Internal works ) ( Concealed work including cutting chases and good the walls etc.) B)20 mm dia pipe nominal OD pipes Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | For Toilet | Mtr | 1 | 125.00 | | | | |
| | | | | | | | 125.00 | |
| | | | | | | Total Work Done | 125.00 | |
| | | | | | | Qty Payable Upto 125 % | 50.00 | |
| | | | | | | Qty Payable Above 125 % | 75.00 | |
| 31 | Providing and fixing in position brass gate valve with C.I wheel of approved quality (screwed end) NB including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. Specification no: KBS 13.2.6/ a) of 20mm dia. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | For Toilet | No's | 28.00 | | | | | |
| | | | | | | | 28.00 | |
| | | | | | | Total Work Done | 28.00 | |
| | | | | | | Qty Payable Upto 125 % | 15.00 | |
| | | | | | | Qty Payable Above 125 % | 13.00 | |
| 32 | Providing and fixing in position brass gate valve with C.I wheel of approved quality (screwed end) NB including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. Specification no: KBS 13.2.6/ b) of 25mm dia. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | For Toilet | No's | 20.00 | | | | | |
| | | | | | | | 20.00 | |
| | | | | | | Total Work Done | 20.00 | |
| | | | | | | Qty Payable Upto 125 % | 10.00 | |
| | | | | | | Qty Payable Above 125 % | 10.00 | |

Contractor Represented

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara Pa

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Date : 30.06.2022

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| 33 | Supplying water storage tanks made of virgin polymer (LLDPE) with two layers outer Black or Blue and inner White layer of approved quality and make, conforming to I.S.I./ISO/SSI specifications. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **For Toilet** | No's | | | | | | |
| | | | 2.00 | 1000.00 | | | | |
| | | | 2.00 | 1500.00 | | | | |
| | | | | | | | 2000.00 | |
| | | | | | | | 3000.00 | |
| | | | | | | **Total Work Done** | 5000.00 | |
| | | | | | | **Qty Payable Upto 125 %** | 1000.00 | |
| | | | | | | **Qty Payable Above 125 %** | 4000.00 | |
| 34 | Providing and fixing to wall, ceiling and floor chlorinated poly vinyl chloride ( CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all cpvc plain and brasss threaded fittings including fixing thepipes with the clamp at . This includes joinihg of pipes fittings with one set of cpvc solvent cement and testing of joints complete (External works ) 25 mm dia pipe nominal OD pipes. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | **For Toilet** | Mtr | | | | | | |
| | | | 1.00 | 30.00 | | | 30.00 | |
| | | | 1.00 | 30.00 | | | 30.00 | |
| | | | 1.00 | 30.00 | | | 30.00 | |
| | | | 1.00 | 30.00 | | | 30.00 | |
| | | | 1.00 | 30.00 | | | 30.00 | |
| | **Pipeline** | | | | | | | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 30.00 | | | 30.00 | |
| | | | 1 | 18.00 | | | 18.00 | |
| | | | | | | **Total Work Done** | 498.00 | |
| | | | | | | **Qty Payable Upto 125 %** | 100.00 | |
| | | | | | | **Qty Payable Above 125 %** | 398.00 | |

Asst. Engineer
Ward No 17

Contractor Represented

Asst. Executive Engineer
Yeshwanthpur Sub Division
Bruhat Bangalore Mahanagara Pa

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

Page : 30.06.2022

Bill Status : 1st And Final Bill

| Sl No | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| | Providing stone ware gully trap of approved quality and fixing in C.C 1:2:4 and plastering with C.M 1:3 where ever necessary (Rate including cost of all materials, fixtures and lead). Size: 15 cm x 10 cm. Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | |
| | For Toilet | Mtr | 20.00 | | | | 20.00 | |
| | | | | | | Total Work Done | 20.00 | |
| | | | | | | Qty Payable Upto 125 % | 20.00 | |
| | | | | | | Qty Payable Above 125 % | 10.00 | |
| 28 | Constructing brick masonry inspection chamber 450x450mm, and 450mm depth, ( clear inside dimension ) for single pipeline, using table moulded non-modular bricks of class designation 50 in cement mortar 1:5, C.I cover with frame (light duty) 455x455 mm internal dimensions, total weight of cover with frame to be not less than 38 kg ( weight of cover 23kg and weight of frame 15 kg) R.C.C. top slab with cement concrete M15 with 20mm and downsize granite metal, foundation concrete M5 with 40mm and downsize granite metal inside plastering 12mm thick with cement mortar 1:3, finish smooth with a floating coat of cement on walls and bed concrete complete as per standard design including cost of materials, labour | | | | | | 10.00 | |
| | For Toilet | No's | 8.00 | | | | 8.00 | |
| | | | | | | Total Work Done | 8.00 | |
| | | | | | | Qty Payable In This Bill | 8.00 | |
| TRL-1 | Providing and fixing self-supported, ribbed, high quality, high grade (D:350 MPAYst Min ), pre- painted Galvalume steel roof sheet, coatedwith bare Galvalume coating AZ 150, @150 gms/Smtr 55%AL,45%Zn)by hot dip process , of total coated thickness as specified for differentspans with a tolerance of+/- 0.02 mm, according to technical specificationconfirming to A 792, with NCCA11-1, or ECCAT4 Pencil hardness HB,NCCA standard T-Bend test. The roof should be fastened to thegutterbeam, on the external sloping side, at an interval of 51mm Centre toCentre, to a depth of 65 mm with Gl anchor bolts and neoprenewashers & subjecting the gutter beam to Schmidt, Hammer test toensure the anchorage of the anchor bolts. The self-supported roofingsystem should be designed to with stand the wind loacl (As per IS 875part-3) & Earthquake load (as per IS 1893) &the design should alsocomply with any other technical requirements such as turbo ventilatorsof 0.60 mts. dia and skylights of size 4.26 x 0.60 mts. fixed one in each row @ 10.00 Mtr C/C alongthe length & hangers for electrical fixturesas per the requirements including cost of all materials &labour forerection, all lead and lift, loading and unloading, HOM of machineriesetc.,complete as per the standard detailed technical specification,design and directions of the engineer in charge of the work. | | | | | | | |
| | For Toilet | No's | 1.00 | 11.65 | 6.35 | | 73.98 | |
| | | | | | | Total Work Done | 73.98 | |
| | | | | | | Qty Payable In This Bill | 73.98 | |

Assistant Engineer
Ward No 17

Contractor Represente

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

04.07.2022

Bill Status : 1st And Final Bill

| Item : | Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|---|
| Sl No | | | | | | | | |
| URL -2 | Fabrication supplying and erecting M.S. tubular trusses of all spans as Kg per approved drawing & design with prefabricated steel applications usingquality material and are durable, reliable and corrosion and abrasionresistant. Welding shall confirm to latest structural welding code. Qualityshall be on various parameters like shape, size, design gauge andpolish. The entire trusses is anchored in RCC column by using 4 nosof M.S. anchor bolts at each support with 10mm thick base plate andshoe plate. The work includes cutting, straightening, placing in positionM.S. pipes and welding wherever necessary and applying one coat ofredoxide primer coat to all the members including cost of all materials,labour charges, and hire charges of machineries for cutting, welding,grinding and erection equipments, with all lead and lift, transportation,letc., complete as per specification | Kg's | | | | | | |
| | **For Toilet** | | | | | | | |
| | MB -150PIPE Vertricle | Kg's | no's | length | wt/m | | | |
| | MB -150PIPE Connecting | | 8.00 | 2.20 | 18.90 | | | |
| | Bracing | | 4.00 | 7.35 | 18.90 | | 332.64 | |
| | MB -150PIPE Purline | | 7.00 | 12.15 | 18.90 | | 555.66 | |
| | For Base Plate | | | | | | 1607.45 | |
| | 20mm thick plate | | 16.00 | 0.56 | 157.00 | | | |
| | For Anchor bolt | | 128.00 | 0.75 | 2.47 | | 1413.00 | |
| | For Gusset Plate | | | | | | 237.12 | |
| | | | | | | | 300.00 | |
| | | | | | | **Total Work Done** | 4445.87 | |
| | | | | | | **Qty Payable In This Bill** | 4438.65 | |
| URL -3 | KSRB 7.1 : Providing and fixing in position collapsible steel shutters Sqm with single or double leaf with vertical channel 20mmx10mmx2mmn braced with flat iron diagonals 20mmx5mm size, with top and bottom rails of T iron sections of 40x40x6 mm with 38mm dia steel pulleys complete with bolt and nuts, locking arrangements, stoppers, handles on both sides with 7.5cms openings at 10 cms. c to c applying a priming coat of red lead paint, cost of materials, labour, HOM complete as per specifications, size of gate 2.4mx1,4m Specification No. KBS 7.7 / 7.12 | | | | | | | |
| | | Sqm | | | | | | |
| | **For Toilet 2 and 3** | | | | | | | |
| | | | 2.00 | 3.30 | | 2.10 | 13.86 | |
| | | | | | | **Total Work Done** | 13.86 | |
| | | | | | | **Qty Payable In This Bill** | 13.86 | |

Contractor Representive

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

04.07.2022

Bill Status : 1st And Final Bill

| Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|
| Providing and fixing M.S. Hand railing for Balcony/Staircase etc., Sqm with 50mm dia. M.S. hollow pipe of 14 gauge, welded to 20mmx20mm M.S. square rod placed vertically, spaced at 100mm at regular intervalsof 600mm. These vertical rods laterally tied to 3 horizontal rods spacedat equal interval. These assembly is fixed to concrete by using expansionbolts and welding the same to reinforcement bars and making good thesurface. All the joints and sections hould be cut to length, welded andgrinded wherever necessary etc., complete. The work includes cost of allmaterials, labour charges for all items of work, hire charges for welding,cutting and grinding equipment, and electricity charges, etc., completeas per specification and drawing. | Kg's | | | | | | |
| For Toilet 1 | | 2.00 | 2.00 | | 1.20 | 4.80 | |
| For Toilet 2 and 3 | | 2.00 | 4.00 | | 1.20 | 9.60 | |
| For Toilet 4 | | 1.00 | 15.70 | | 1.20 | 18.84 | |
| | | 2.00 | 9.00 | | 1.20 | 21.60 | |
| | | | | Total Work Done | | 54.84 | |
| | | | | Qty Payable In This Bill | | 54.84 | |
| SR -5 Supplying and fixing new Mangalore tiles on existing reepers including cost of materials, labour, HOM complete as per specifications. | Sqm | | | | | | |
| For Toilet 1 And 2 | | 4.00 | 5.70 | 3.30 | | 75.24 | |
| For Toilet 3 | | 2.00 | 4.85 | 5.80 | | 56.26 | |
| | | | | Total Work Done | | 131.50 | |
| | | | | Qty Payable In This Bill | | 131.50 | |

Contractor Represented

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara Palike

Scanned with CamScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

MEASUREMENT SHEET

**Name of Work:- Construction of Toilets Insides JP Park In Ward No 17**

04.02.2022

Bill Status : 1st And Final Bill

| Description of Items | Unit | No | L (M) | B (M) | D (M) | Qty | Remarks |
|---|---|---|---|---|---|---|---|
| Providing and fixing M.S. Grill over existing compound wall as per using 16mm x 16mm M.S. Square rod at 150mm c/c spacing and 6mm x 40mm M.S. flats at horizontal and 6mm x12mm M.S flat for ornamental design and providing shop edge design at -thevertex of every vertical rods, including welding, grinding wherevernecessary. All the steel surface should be thoroughly cleanedfree of rust and painted with anti corrosive paint (shop paint) etc.,complete. The work includes cost of all materials, labour chargesfor all items of work, hire charges for welding, cutting and grindingequipment, and electricity charges, etc., complete as per specification. | | | | | | | |
| | Sqm | | | | | | |
| For Toilet 1 | | | | | | | |
| Above Wall | | 1.00 | 32.00 | | 1.50 | 48.00 | |
| | | | | | Total Work Done | 48.00 | |
| | | | | | Qty Payable In This Bill | 48.00 | |
| Providing and fixing M.S. Gate as per Chief Architect Drawing,ornamental shape as shown in the drawing and 35mm x 6mm and 16 x16mm Square rods for verticals alternatively spaced at 4cms c/c in twohalves and 40mmx6mm M.S. flats for horizontal member and at the topcast iron spikes are provided at alternate vertical members as shown inthe drawing etc., complete. All the steel surface should be thoroughlycleaned free of rust and painted with anti corrosive paint (shop paint) etc.,complete. The work includes cost of all materials, labour charges for allitems of work, hire charges for welding, cutting and grinding equipment,and electricity charges with lead and lift, loading and unloading charges,etc., complete as per specification. | | | | | | | |
| | Sqm | | | | | | |
| Above Wall | | 1.00 | 3.30 | | 2.10 | 6.93 | |
| | | | | | Total Work Done | 6.93 | |
| | | | | | Qty Payable In This Bill | 6.93 | |

Contractor Representive

Ass. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara Palike

Scanned with CamScanner

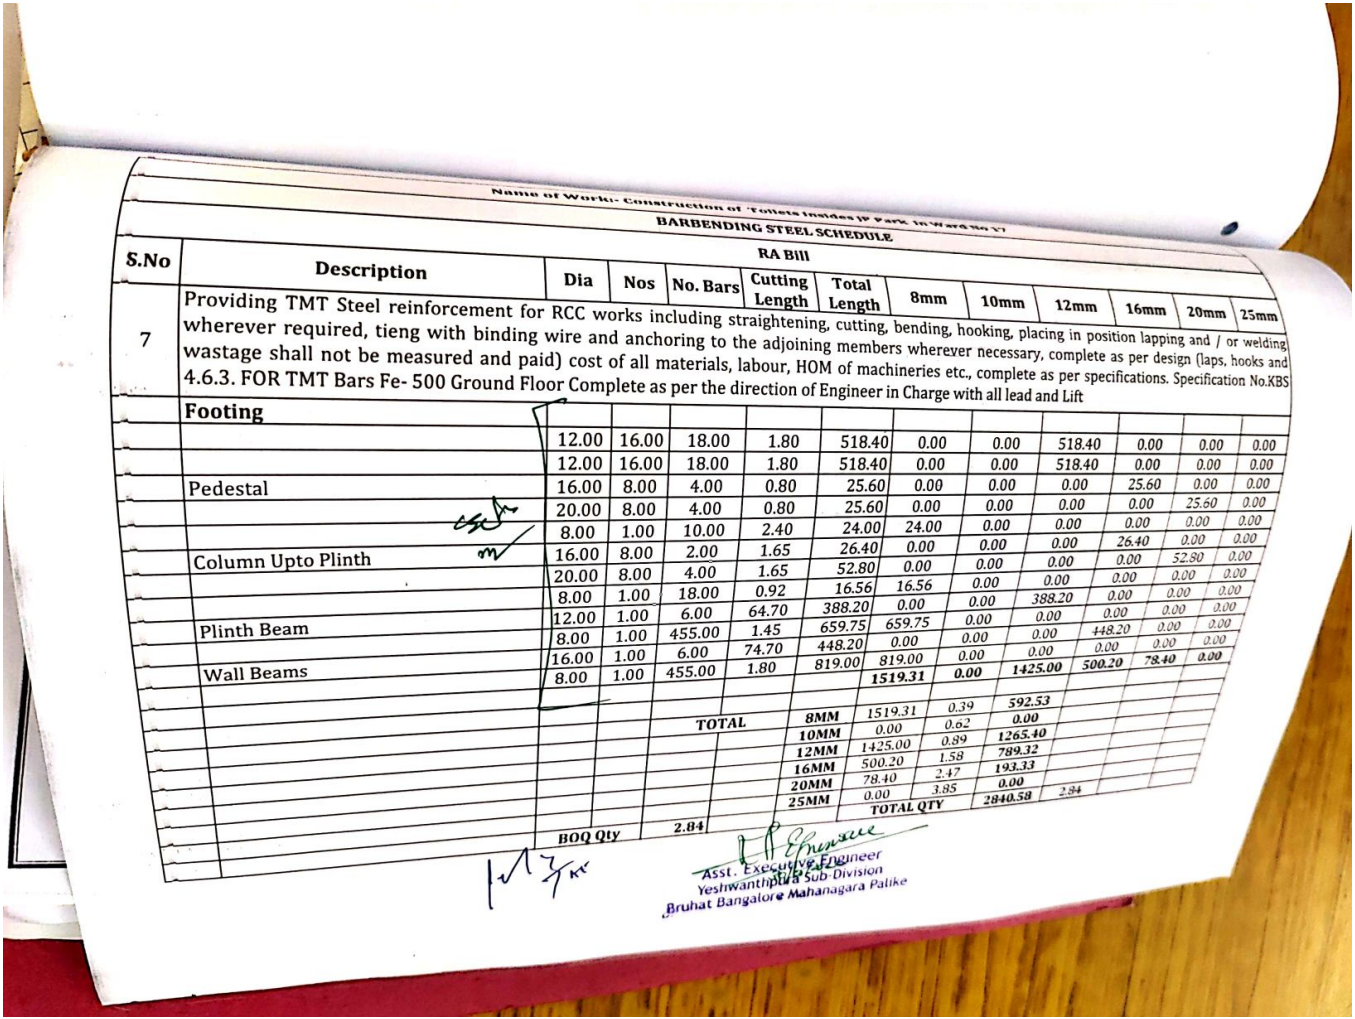

Name of Work:- Construction of Toilets Inside JP Park in Ward No 27

## BARBENDING STEEL SCHEDULE

RA Bill

| S.No | Description | Dia | Nos | No. Bars | Cutting Length | Total Length | 8mm | 10mm | 12mm | 16mm | 20mm | 25mm |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 7 | Providing TMT Steel reinforcement for RCC works including straightening, cutting, bending, hooking, placing in position lapping and / or welding wherever required, tieng with binding wire and anchoring to the adjoining members wherever necessary, complete as per design (laps, hooks and wastage shall not be measured and paid) cost of all materials, labour, HOM of machineries etc., complete as per specifications. Specification No.KBS 4.6.3. FOR TMT Bars Fe- 500 Ground Floor Complete as per the direction of Engineer in Charge with all lead and Lift | | | | | | | | | | | |
| | **Footing** | | | | | | | | | | | |
| | | 12.00 | 16.00 | 18.00 | 1.80 | 518.40 | 0.00 | 0.00 | 518.40 | 0.00 | 0.00 | 0.00 |
| | | 12.00 | 16.00 | 18.00 | 1.80 | 518.40 | 0.00 | 0.00 | 518.40 | 0.00 | 0.00 | 0.00 |
| | Pedestal | 16.00 | 8.00 | 4.00 | 0.80 | 25.60 | 0.00 | 0.00 | 0.00 | 25.60 | 0.00 | 0.00 |
| | | 20.00 | 8.00 | 4.00 | 0.80 | 25.60 | 0.00 | 0.00 | 0.00 | 0.00 | 25.60 | 0.00 |
| | | 8.00 | 1.00 | 10.00 | 2.40 | 24.00 | 24.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| | Column Upto Plinth | 16.00 | 8.00 | 2.00 | 1.65 | 26.40 | 0.00 | 0.00 | 0.00 | 26.40 | 0.00 | 0.00 |
| | | 20.00 | 8.00 | 4.00 | 1.65 | 52.80 | 0.00 | 0.00 | 0.00 | 0.00 | 52.80 | 0.00 |
| | | 8.00 | 1.00 | 18.00 | 0.92 | 16.56 | 16.56 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| | Plinth Beam | 12.00 | 1.00 | 6.00 | 64.70 | 388.20 | 0.00 | 0.00 | 388.20 | 0.00 | 0.00 | 0.00 |
| | | 8.00 | 1.00 | 455.00 | 1.45 | 659.75 | 659.75 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| | | 16.00 | 1.00 | 6.00 | 74.70 | 448.20 | 0.00 | 0.00 | 0.00 | 448.20 | 0.00 | 0.00 |
| | Wall Beams | 8.00 | 1.00 | 455.00 | 1.80 | 819.00 | 819.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| | | | | | | | 1519.31 | 0.00 | 1425.00 | 500.20 | 78.40 | 0.00 |

| | | | | |
|---|---|---|---|---|
| | TOTAL | 8MM | 1519.31 | 0.39 | 592.53 |
| | | 10MM | 0.00 | 0.62 | 0.00 |
| | | 12MM | 1425.00 | 0.89 | 1265.40 |
| | | 16MM | 500.20 | 1.58 | 789.32 |
| | | 20MM | 78.40 | 2.47 | 193.33 |
| | | 25MM | 0.00 | 3.85 | 0.00 |
| | | | TOTAL QTY | | 2840.58 |
| | BOQ Qty | 2.84 | | | 2.84 |

Asst. Executive Engineer
Yeshwanthpura Sub-Division
Bruhat Bangalore Mahanagara Palike

Scanned with CamScanner
